



Interreg

Latvija-Lietuva

European Regional Development Fund



EUROPEAN UNION

LLI-10 Introducing nature tourism
for all

UniGreen

JAURYKLA PARK IN KRETINGA



2nd PERIOD OVERVIEW




2nd PERIOD OVERVIEW

On October 10th, 2017 Kretinga Municipality administration first time suspends the contract for the implementation works of the Jaurykla park because at the time of contract it was not possible to foresee frequent and heavy rain, the soaked soil, the rising Jaurykla river and the groundwater level. Despite the weather and extreme situation, all works was planning to finish in second period, but winter came and all works were stoped again. Most of the planned work is already started in the park, but due to bad weather, they did not manage to 100%. finish by the end of the second period. At this moment, it is planned that works will be finalized on May 23, 2018.


2nd PERIOD OVERVIEW

In accordance with public procurement procedures on August-October 2017, was purchased the equipments to Playground for 1-6 year olds children and Adventure park for 7-15 year olds children. In the spring of 2018 these equipments were installed in the Jaurykla park.

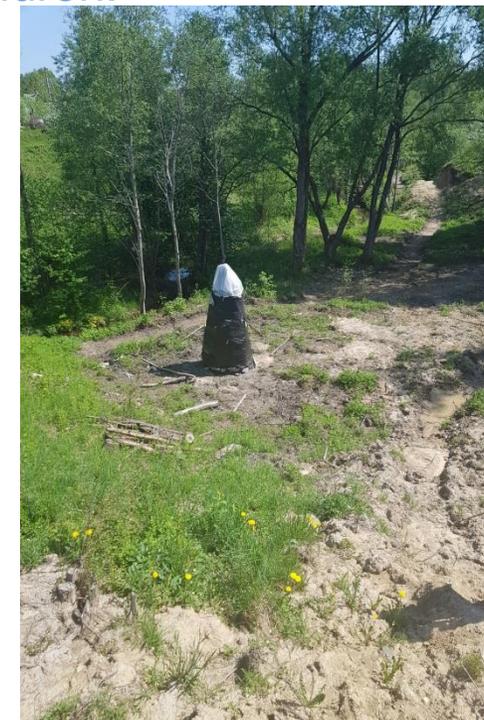

2nd PERIOD OVERVIEW


The situation is these days:

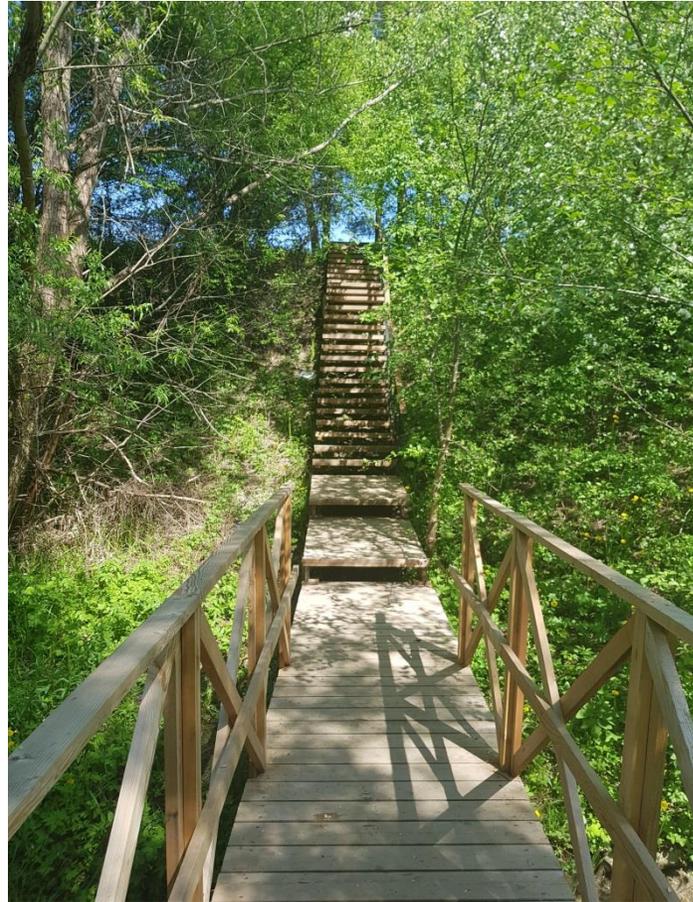

JAURYKLA PARK IN KRETINGA



JAURYKLA PARK IN KRETINGA

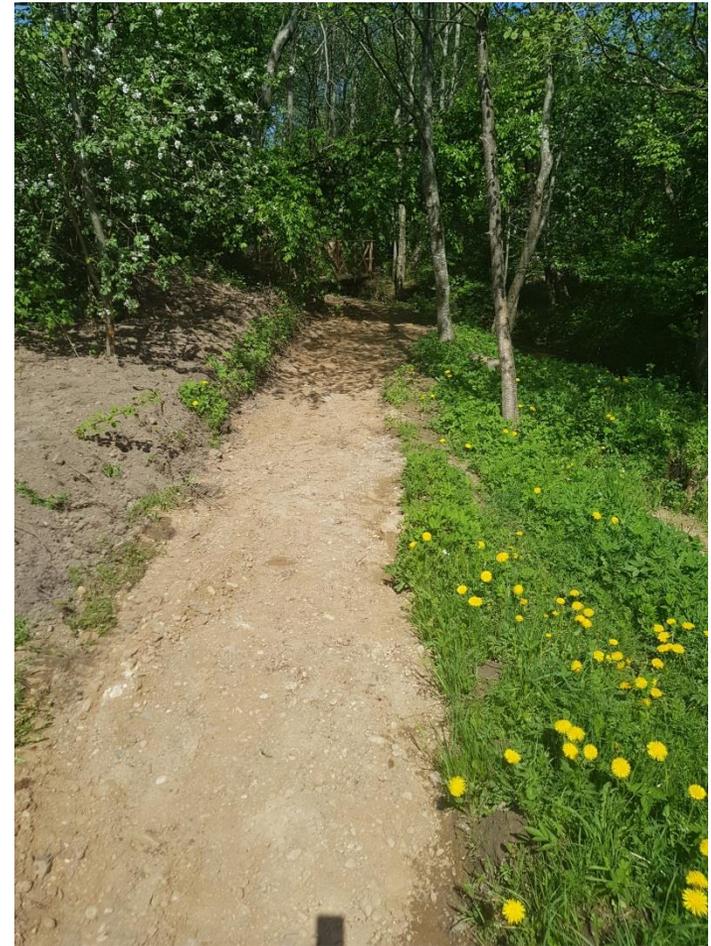

2 nd PERIOD OVERVIEW

The end 😊
