

# LLI-010 Introducing nature tourism for all **UniGreen**

## **Activity schedule & delivery dates for Period 2** **November 2017 – April 2018**



Alise Lūse  
Project Manager



The project is co-financed by the  
Interreg V-A Latvia - Lithuania Cross Border Cooperation Programme 2014–2020  
[www.latlit.eu](http://www.latlit.eu)

Activities			Period 1 (01.05.17.-31.10.17.)													
			May		June		July		August		September		October		November	
			D	P	D	P	D	PP	D	PP	D	P	D	P	D	PP
WP Management (M)																
Activity	M.1	Kick-off			M.1.1	LP										
					M.1.2	LP										
Activity	M.2	PMMs													M.2.1	LP
Activity	M.3	Reporting														
WP Nature access for all (I1)																
Activity	I1.1	Seaside trail in Roja											I1.1.1	PP7	I1.1.2	PP7
															I1.1.3	PP7
Activity	I1.2	Watching tower near Sātiņi ponds														
	I1.4	Tourism infr. to improve Durbe lake access														
Activity																
Activity	I1.5	Trail along Venta in Skrunda											x	PP9		
Activity	I1.6	Trail along Venta in Kuldīga														
Activity	I1.7	Trail along Usma lake													I1.7.1	PP10
Activity	I1.8	Jaurykla park in Kretinga					I1.8.2	PP5			I1.8.1	PP5				
											I1.8.3	PP5				
							I1.8.4	PP5								
											I1.8.5	PP5				
											I1.8.6	PP5				
											I1.8.7	PP5				
											I1.8.8	PP5				
											I1.8.9	PP5				
											I1.8.10	PP5				
											I1.8.11	PP5				
											I1.8.12	PP5				
											I1.8.13	PP5				
											I1.8.14	PP5				
											I1.8.15	PP5				
Activity	I1.9	Tourism infr. to improve access in Kirkilai karstic lake in Biržai Regional Park														
Activity	I1.10	Tourism infr. improved for people with disabilities in Aukštaitija National Park														
Activity	I1.11	Viewing platform in Plateliai											x	PP11		
WP Competence&promotion (T1)																
Activity	T1.1	Trainings&workshops to adopt tourism infrastructure and services for people with disabilities			x	LP										
Activity	T1.2	Learning best practice							T1.2.3	LP						
											T1.2.2	LP				
											T1.2.4	PP11				
Activity	T1.3	Marketing activities to promote nature tourism possibilities											x	LP		
WP Communication (C)																
Activity	C.1	Promotional materials	C.1.1	LP												
Activity	C.2	Digital activities	C.2.1	All												

Not accomplished

[illegible]

# Deliverables - LP

WP Management, WP Competence & promotion, WP Communication  
 Activities: PMMs (M.2), Trainings&workshops (T.1.1)

Deliverable No.	Deliverable title	Target value	Delivery date
M.2.1	Participants in PMM 1	30	01.11.2017
M.2.2	Participants in PMM 2	30	01.04.2018
M.3.1	FLC confirmation on Report 1	12	01.01.2018
T1.1.5	Participants at 2 workshops in Kurzeme	60	01.05.2018


# LP – Activity T.1.1 Trainings&workshops

- **2 workshops in Kurzeme** for entrepreneurs and municipal tourism specialists on specific needs of people with disabilities

**Deliverable T1.1.5**

**Liepāja & Roja?**

**To be organised in April 2018**

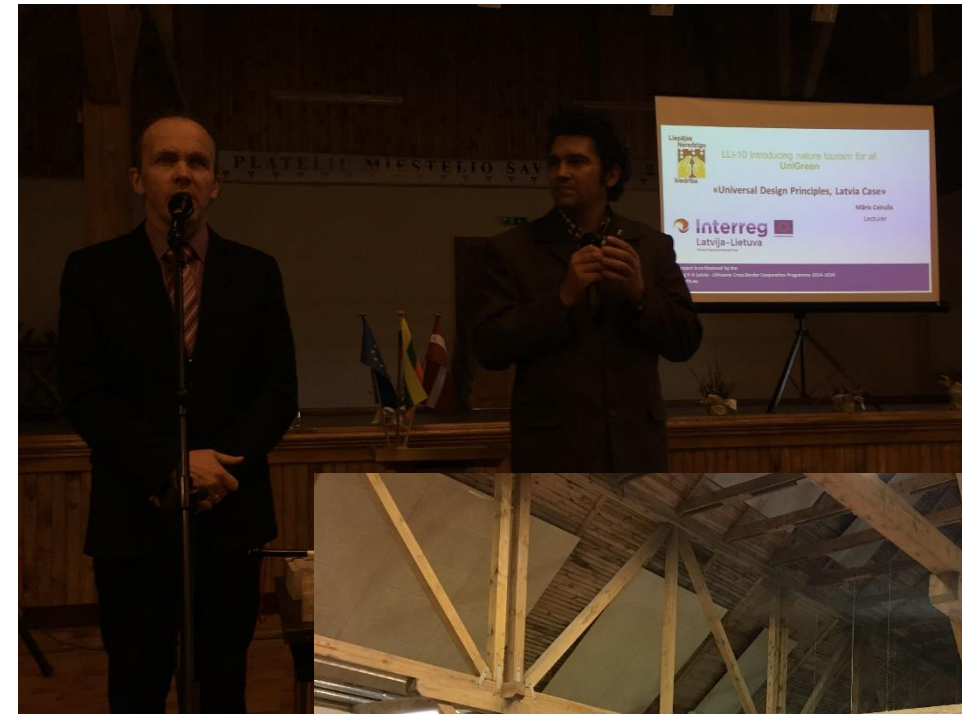

# LP – other activities started

- **Training of nature guides**

**Deliverable T1.1.1**

**27 selected**

1. Conference in Plateliai

19-20 October 2017

2. 6 training sessions in Kurzeme

First 09.-11.11.17. in Kuldīga

Second 18.-20.01.18. in

Finishing on 30.11.18.



**Be a better guide**

# LP – other activities started

- **On-spot checks for trail maps & image guide**

To select the trails for inspection → set criteria  
→ round trips → trails mapped by 28.09.18.



Trail maps → 28.12.18.

LP – 30 walking trails

PP2 → 4 water routes

PP3 → 4 trails

PP5 → 5 trails

PP11 → 4 trails

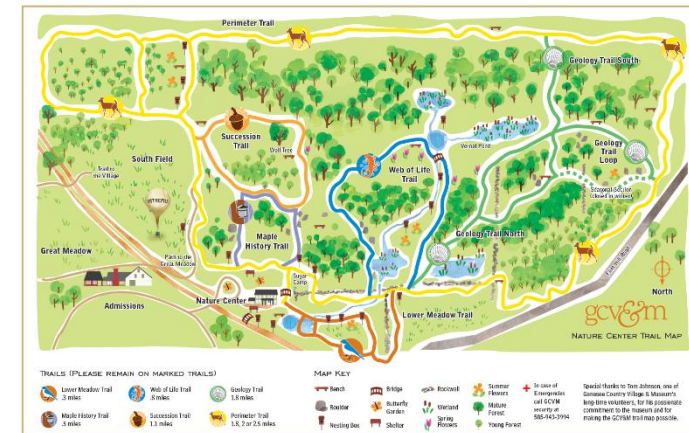


Image guide (LV, LT, ENG) → 20000 copies →  
28.01.19.

# Deliverables – PP3 (Biržai)

WP Competence & Promotion

Activities: Marketing (T1.3)

Deliverable No.	Deliverable title	Target value	Delivery date
T1.3.6	QR codes with and audio material (LT, LV, ENG)	3	28.02.2018

# Deliverables – PP5 (Kretinga)

WP Nature access for all

Activities: Jaurykla park in Kretinga (I1.8)

Deliverable No.	Deliverable title	Target value	Delivery date
I1.8.1	Amphitheater	1	01.09.2017
I1.8.2	Wellness trail with recreational equipment	1	01.07.2017
I1.8.3	Recreational area with benches and dustbins	9	01.09.2017
I1.8.4	Education nature trail	1	01.07.2017
I.1.8.5	Landscape image viewing platform	4	01.09.2017
I.1.8.6	Swings	5	01.09.2017
I.1.8.7	Reflexotherapy trail	1	01.09.2017
I.1.8.8	Stainless steel slide	1	01.09.2017
I.1.8.9	Playground with various gaming equipment designed for 1-6 year old children	1	01.09.2017
I1.8.10	Information stand	4	01.09.2017
I.1.8.11	Special trail come down to people with disabilities problems	1	01.09.2017

# Deliverables – PP5

WP Nature access for all

Activities: Jaurykla park in Kretinga (I1.8)

Deliverable No.	Deliverable title	Target value	Delivery date
I1.8.12	Wooden stairs with handrails adapted to people with visibility problems	1	01.09.2017
I1.8.13	Small bridge and foot-bridge	6	01.09.2017
I1.8.14	Toilets	3	01.09.2017
I1.8.15	Adventure park for 7-15 year old children	1	01.09.2017

# Deliverables – PP5

WP Competence & Promotion

Activities: Learning best practice (T1.2)

Deliverable No.	Deliverable title	Target value	Delivery date
T1.2.1	Participants in experience exchange visit in Kurzeme	1	01.04.2018

↓  
05.2018

# Deliverables – PP7 (Roja)

WP Nature access for all

Activities: Seaside trail in Roja (I1.1)

Deliverable No.	Deliverable title	Target value	Delivery date
I1.1.2	Information stand	1	01.11.2017
I1.1.3	Visitor counter	1	01.11.2017

# Deliverables – PP8 (Saldus)

WP Nature access for all

Activities: Watching tower near Sātiņi ponds (I1.2)

Deliverable No.	Deliverable title	Target value	Delivery date
I1.2.1	Watching tower	1	01.12.2017
I1.1.3	Information stand and warning signs	1	01.12.2017

Done

# Deliverables – PP10 (Ventspils)

WP Nature access to all

Activities: Trail along Usma lake (I1.7)

Deliverable No.	Deliverable title	Target value	Delivery date
I1.7.1	Trail	1	01.11.2017
I1.7.2	Visitor Counter	1	28.04.2018

# Deliverables – PP11 (Žemaitija)

WP Nature access to all

Activities: Viewing platform in Plateliai (I1.11)

Deliverable No.	Deliverable title	Target value	Delivery date
I1.11.1	Platform	1	01.02.2018
I1.11.3	Information stands	9	01.02.2018
I1.11.4	Visitor counter	1	01.02.2018

# Deliverables – PP11 (Žemaitija)

WP Competence & Promotion

Activities: Trainings & workshops (T.1.1)

Deliverable No.	Deliverable title	Target value	Delivery date
T1.1.2	Trained tour guides for LT participants	15	01.04.2018
T1.1.3	Educational programs for participant guides and target group	2	01.04.2018
T1.1.4	2 practical trainings	2	01.04.2018
